

STRICTLY PRIVATE AND CONFIDENTIAL

Green Square

Commercial and office development, El Mostakbal City, Cairo

Private placement: investor ticket of EGP 50 million

ALL INFORMATION IN THIS PRESENTATION IS CONFIDENTIAL AND SUBJECT TO THE NON-DISCLOSURE AGREEMENT. Do not copy, forward or disclose it.

Investment highlights

13,023 m2

Built-up area, G+2: 4,341 m2 retail and 8,682 m2 offices

Month 48

Handover; sales from month 7, construction from month 13 for 36 months

EGP 2.25 bn

Sales plan: 80% of units sold over the sales window, at modelled prices

35 / 65

Revenue split between the landowner (Al Ahly Sabbour) and Jalour

- Land owned by Al Ahly Sabbour; Jalour designs, permits, builds (core and shell), markets, sells, collects and operates.
- Landlord receives 35% of collections with a minimum guarantee of EGP 800 million over six years; Jalour keeps 65%.
- Option A: units with a face value of EGP 100 million (2.0x the ticket) at launch list prices. Projected investor IRR 26.4% (base).
- Option B: cash return of EGP 115 million (2.3x the ticket) in 12 quarterly instalments after a 24-month grace period. Projected investor IRR 26.5%.
- Project-level exposure only: the investment has no exposure to other Jalour projects.

Source: Jalour financial model; Financial Annex, Summary sheet. IRRs are projections, not guarantees.

Transaction overview

Term	Summary
Investor ticket	EGP 50 million (USD 1.0 million at EGP 48 per USD)
Issuer	Project company for this development (name, jurisdiction and instrument to be confirmed by counsel)
Use of proceeds	Down payment to the landowner, guarantee instalments and working capital to the funding peak, and pre-construction costs (total modelled need EGP 113.0 million)
Option A: units	Units with a face value of EGP 100 million at launch list prices, allocated from the first two sales tranches; resale rights subject to consents
Option B: cash	EGP 115 million in 12 equal quarterly instalments of EGP 9.58 million; first payment month 30, last month 63
Choice	The investor chooses Option A or Option B at signing
Balance of funding	The balance of project funding is provided by Jalour sponsor equity, project collections and other capital sources.
Further capital	Jalour may raise further capital at project or holding level, subject to the investor's stated rights (ranking, collateral, information rights)

Source: Term summary; final terms are set by the definitive agreements.

Market: Cairo office and commercial supply and demand

73%

of Cairo office stock, current and future, is in New Cairo

~9%

office vacancy, stable (Q1 2026); Grade A occupancy about 90%

+82%

office pipeline to 2029 relative to current stock: supply is the main risk

USD 348

Grade A rent per m2 per year in New Cairo business parks (Q2 2026)

- Mostakbal City covers about 11,000 feddans, with a planned population of about 1 million; master developer is the state-linked Mostakbal for Urban Development (MIDAR).
- Connected by the Regional (Middle) Ring Road and the East Cairo monorail corridor to Shorouk, Obour, Badr and the New Administrative Capital.
- Cairo retail stock above 3.3 million m2 after about 89,000 m2 delivered in Q1 2026, mostly small malls in New Cairo and Giza; about 331,300 m2 more due by end 2026.
- Comparable commercial schemes are under way: Hassan Allam's HAPTOWN (offices G+1 to G+4, retail, healthcare) in Mostakbal City.

Source: Knight Frank (via Arabian Business, Jul 2026; Enterprise, Jul 2026); JLL Q1 2026 (via Invest-Gate); MIDAR; Nawy; Bayut; Invest-Gate. Knight Frank and JLL use different office-stock definitions.

Market: pricing evidence and demand drivers


Indicator	Evidence	Model assumption
Office prices	Mostakbal City listings: EGP 106,000 to 120,000 per m2 (asking)	Launch EGP 135,000 per m2, rising to 200,000 at the delivery list
Retail prices	New Cairo listings: EGP 139,000 to 325,000 per m2 (asking, individual listings)	Launch EGP 225,000 per m2, rising to 300,000
Price growth	New Cairo secondary prices +3.1% y/y (Q1 2026); broker estimates 10 to 16% a year for 2026	Launch to delivery list: +33% retail, +48% offices; offices +77% on today's asking, about 15% a year
Interest rates	CBE overnight deposit rate 19.00% (Sep 2026); urban inflation 14.5% (Aug 2026)	Discount rate 14% in the model
Developer sales	Top 10 developers EGP 670 bn in H1 2026, +2.9% y/y; units sold -5%	Sales over about 3 years from launch
Payment plans	Typically 8 to 12 years with 1.5% to 10% down payment	Down payments 5% to 20%; instalments 2 to 8 years

Reading across: the sales plan needs price growth that sits at the upper end of recent evidence. The downside case on slide 14 tests lower prices and later sales.

Source: Property Finder listings (2026); JLL via Enterprise (2026); Sands of Wealth (2026); CBE via Bnok24; CAPMAS via Ahram Online; Daily News Egypt; Bayut. Listings are asking prices, not transactions.

The project

Item	Detail
Land area	14,470 m2
Footprint (30%)	4,341 m2
Height	G+2
Retail built-up area	4,341 m2
Office built-up area	8,682 m2
Total built-up area	13,023 m2
Finishing standard	Core and shell
Sales start	Month 7
Construction	Month 13 to 48 (36 months)
Handover	Month 48

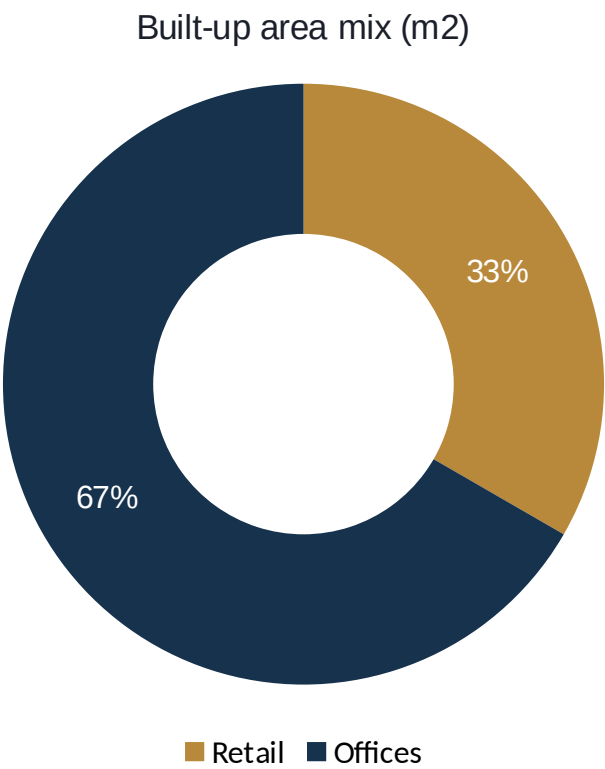

Source: Jalour financial model (project summary). Jalour retains 20% of units, outside the sales plan and outside this offering.

Partnership with Al Ahly Sabbour and the revenue share


Al Ahly Sabbour

Landowner. Receives 35% of collections, subject to a minimum guarantee.

Jalour

Developer and operator. Keeps 65% of collections. Carries design, permits, core-and-shell construction, marketing, sales, collection and operation costs.

Minimum guarantee schedule (EGP million)

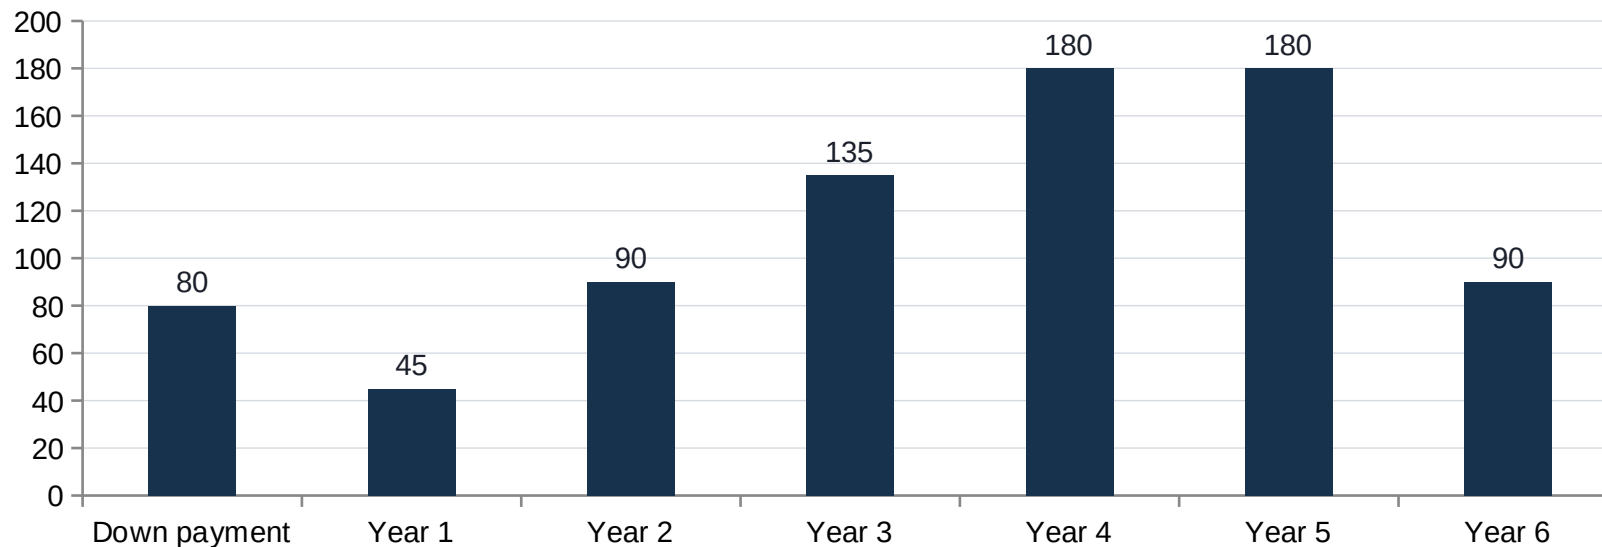

- Minimum guarantee EGP 800 million over six years; down payment EGP 80 million (10%) paid up front.
- Landlord share is 35% of collections or the guaranteed instalment, whichever is higher.
- Any excess of 35% over the guarantee is settled from year 8.
- Allocation of units, assignment of collections or any encumbrance affecting the landlord share requires the landlord's written consent.

Source: Jalour financial model (landlord terms); agreement terms to be confirmed in the data room.

Jalour Developments: role and track record

Role in this project


- Design and permits
- Construction to core-and-shell standard
- Marketing, branding and sales
- Collection of instalments
- Operation, management and maintenance, directly or through a facility management company
- Covers project funding gaps from its cash reserves and cash from other projects it is constructing (to be documented)

Track record and team

- Completed projects, area delivered and units handed over
- Management team biographies
- Audited financial statements of Jalour and Al Jalal Holding
- References from landlords, contractors and buyers
- All provided after the investor signs a non-disclosure agreement

Source: Jalour Developments is the real estate arm of Al Jalal Holding, Cairo. Sponsor materials are provided after the investor signs a non-disclosure agreement.

Sales plan and pricing

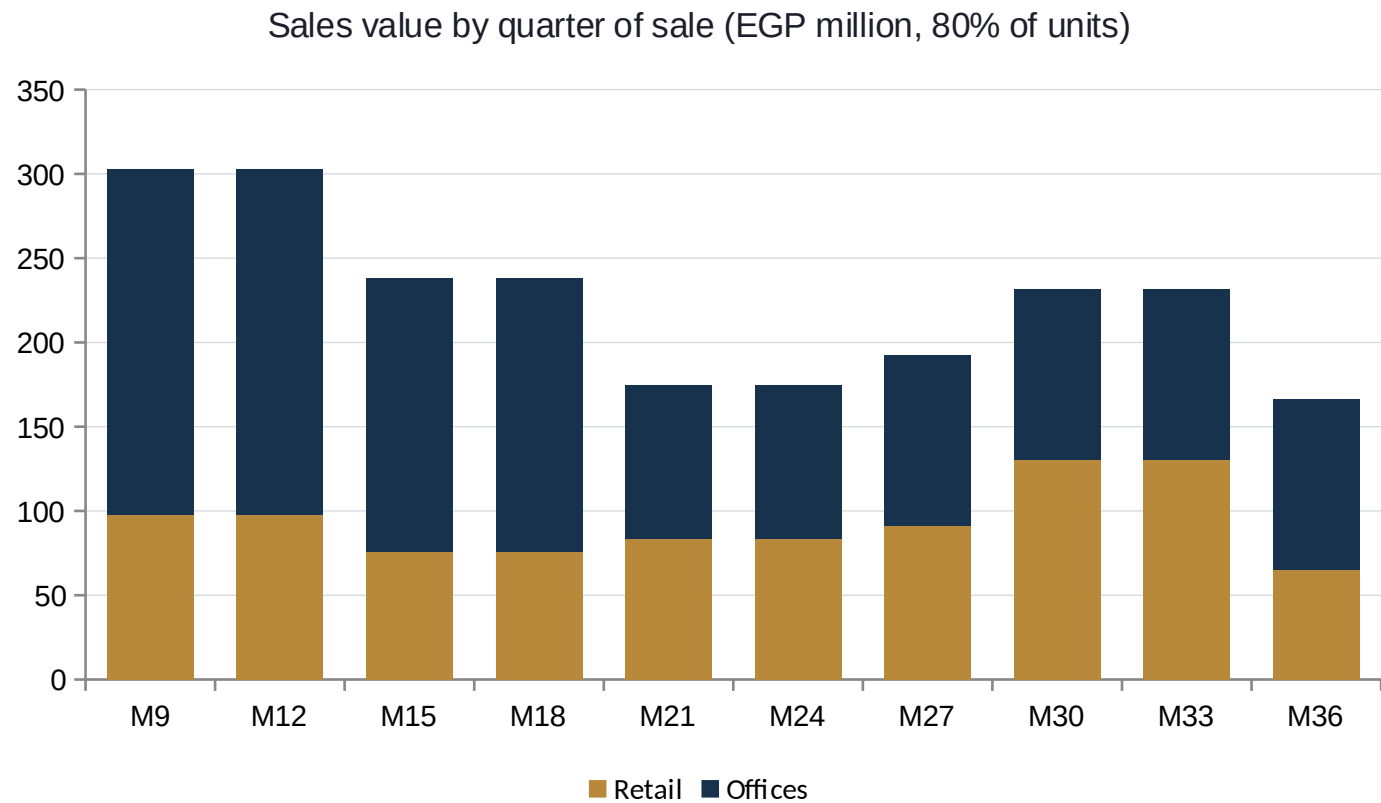


EGP thousand per m2	Launch	Delivery list	Average
Retail	225	300	268
Offices	135	200	163

- Total sales at 100% of units: EGP 2,816 million; plan sells 80%: EGP 2,253 million.
- Payment plans: down payment 5% to 20%, a second equal payment three months later, instalments of 2 to 8 years and a delivery payment of 20% to 25%.
- Delivery payments are collected on a contractual milestone ahead of handover (see risks).

Source: Jalour financial model (sales sheet). Prices are model assumptions; see slide 5 for market evidence.

Collections, costs and cash flow

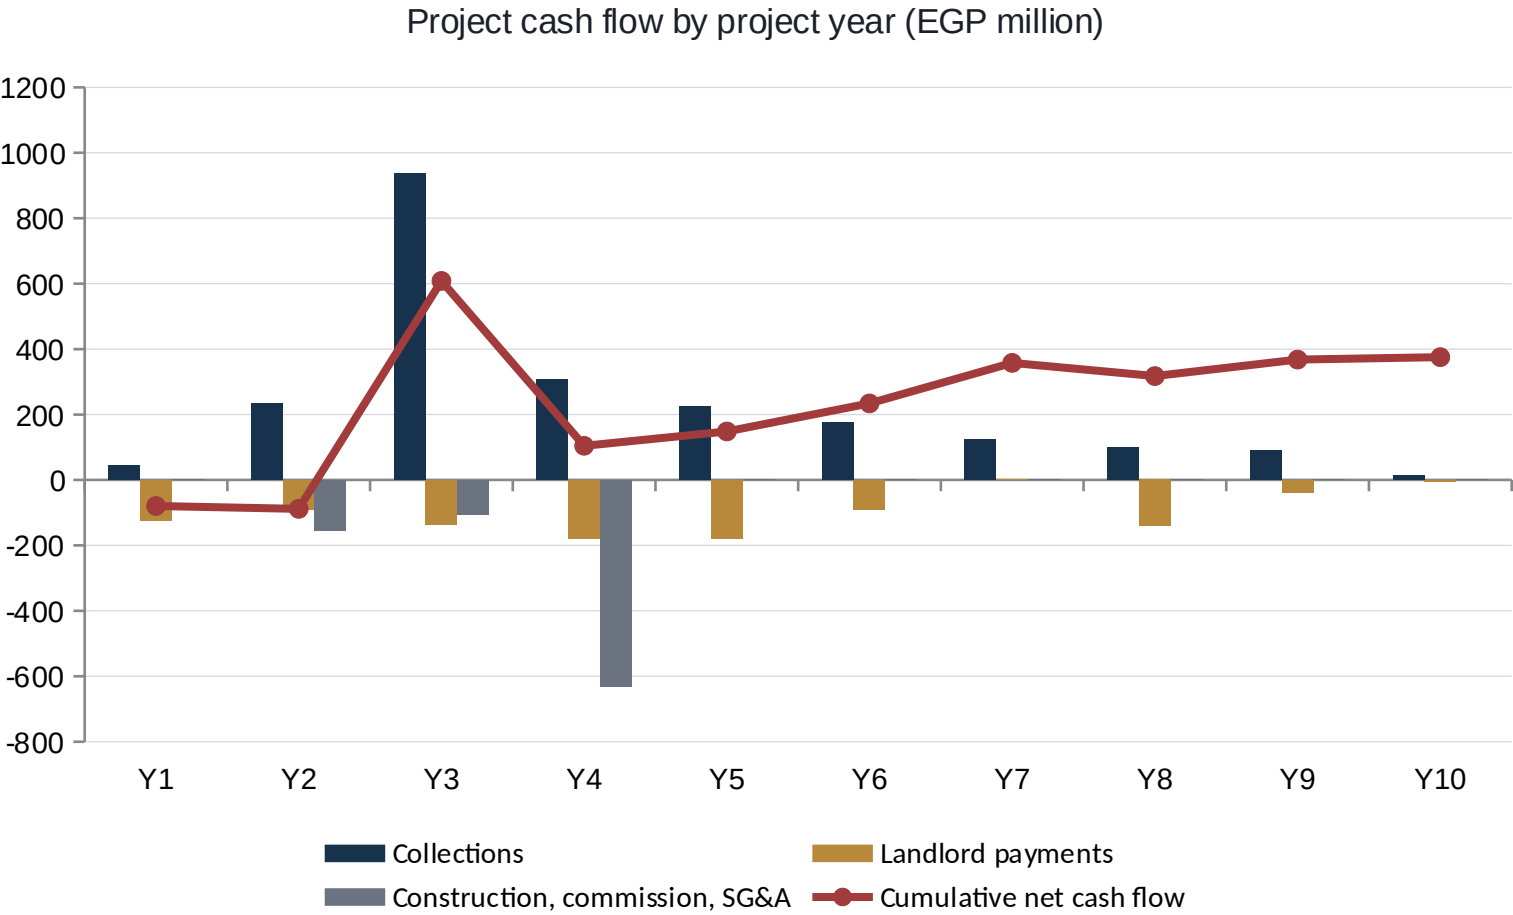

375

Jalour net cash flow, nominal, EGP million

215

NPV at 14%, EGP million

102.5

Peak cumulative shortage, EGP million (month 6)

Source: Jalour financial model; Financial Annex, Project_CF sheet. Project years: Y1 = months 1 to 12. Excludes the 20% of units retained by Jalour.

Sources and uses of funds

Uses	EGP million
Down payment to landowner	80.0
Guarantee instalments and working capital to the funding peak	22.5
Design, permits and pre-construction (assumption)	10.5
Total uses at peak	113.0

Sources	EGP million	% of uses
Investor ticket	50.0	44%
Balance of project funding	63.0	56%
Total sources	113.0	100%

- The balance of project funding is provided by Jalour sponsor equity, project collections and other capital sources.
- Modelled peak cumulative shortage EGP 102.5 million; the ticket is 49% of it.
- If delivery payments arrive at handover the peak shortage is EGP 269 million; if sales slip 12 months with prices 10% lower it is EGP 441 million. Jalour will cover gaps above project cash from its cash reserves and cash from other projects it is constructing.
- Nothing in this structure is ring-fenced: the ticket is project funding.

Source: Financial Annex, Sources_Uses sheet. Pre-construction cost is an assumption pending Jalour's budget.

Option A (units) and Option B (cash) side by side

	Option A: units	Option B: cash
Entitlement	Units with a face value of EGP 100 million (2.0x) at launch list	EGP 115 million (2.3x) in cash
Timing	Allocation at signing; handover month 48; resale from month 51	Grace 24 months; 12 quarterly instalments, months 30 to 63
Price exposure	Yes: value moves with Mostakbal City prices (delivery list 1.43x launch)	No unit price exposure; fixed instalments
Projected IRR, base	26.4%	26.5%
Projected multiple, base	2.78x	2.30x
Upside IRR	29.2% (3.06x)	Contractual: 26.5% if paid
Downside IRR	18.6% (2.50x)	Contractual: 26.5% if paid; depends on Jalour funding
Payback	Month 54	Month 45
Main risk	Resale price and timing; consents to assign	Payment capacity during the construction peak

Source: Financial Annex, Option_A and Option_B sheets. Projections; downside = sales delayed 12 months and prices 10% lower.

Security package and investor protections

Proposed base package


- Option A: a registered allocation of specific units from the first two sales tranches; the units are the investor's asset
- Option B: earmark of specific unsold units with a list value of at least the ticket, with a right to substitute equal value
- Payment priority covenant: no shareholder distributions or shareholder-loan repayments while an instalment is overdue
- Negative pledge on the earmarked units
- Information rights: monthly reporting and audit rights
- Sponsor funding undertaking for project gaps from Jalour cash reserves and other projects' cash; no guarantee of return

Optional and for counsel

- Promissory note or post-dated cheques for each Option B instalment (common practice in Egypt)
- Independent engineer reporting on construction progress
- Step-in right to market the earmarked units after a payment default
- Landlord acknowledgement of the unit allocation
- Parent guarantee: not offered in this structure

Source: Proposal for review by Jalour's lawyers. Landlord consent is required for any allocation or encumbrance affecting its 35% share.

Returns and sensitivity

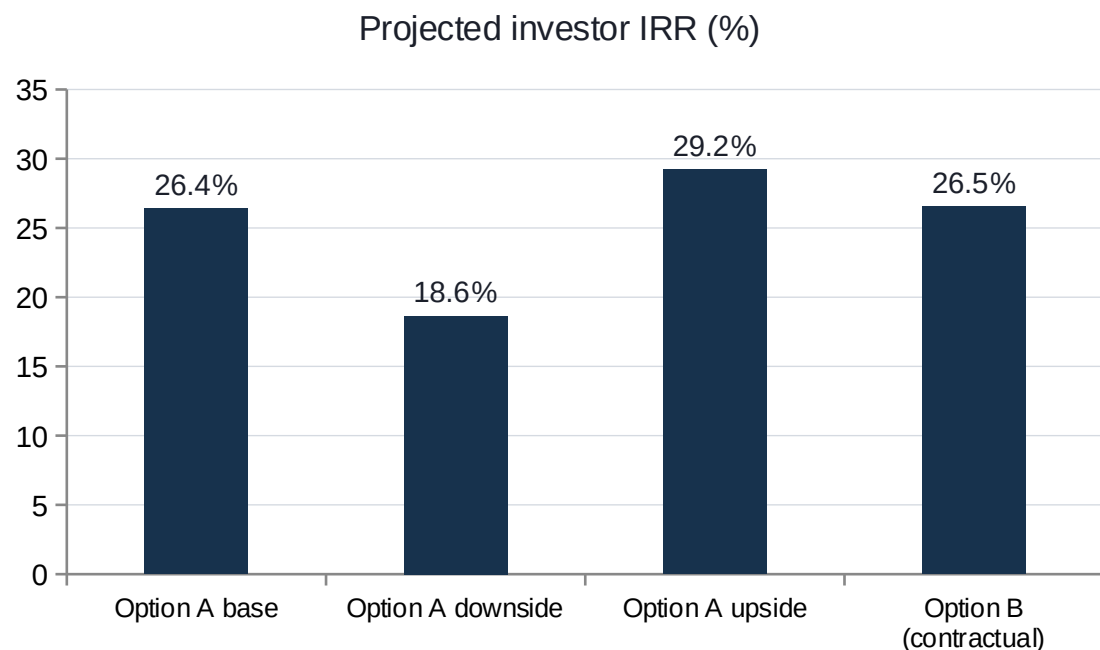

Project case	NPV (EGP m)	Peak shortage (EGP m)
Base	215	103
Prices -10%	116	114
Prices +10%	315	103
Sales delay 12 months	49	408
Cost overrun +10%	162	103
Collections slip 2 quarters	125	236
Delivery payments at handover	155	269

- Option A break-even: the units could be resold at 36% of the delivery list price before the ticket is lost.
- Option B: cash available covers each instalment at least 10.1x on a pooled-cash basis; net cash flow alone covers it in 6 of 12 quarters because of the construction peak.
- Returns are projections, not guarantees.


Source: Financial Annex, Scenarios, Sensitivity and Option sheets. Project cases show Jalour net cash flow before any investor instrument.

Risks and mitigants

Risk	Mitigant
Market and price: sales plan assumes list-price rises of 33% to 48% over the sales window	Downside case shown; Option B has no unit price exposure; price evidence in the data room
Delivery payments collected ahead of handover	Contractual milestone; Jalour covers any gap from cash reserves and other projects' cash; stress case shown
Construction cost and inflation (costs flat in the model)	Cost +10% case; fixed-price contracting to be sought; contingency 5% in the model
Landlord: consent and minimum guarantee payments	Written consent as a condition precedent; guarantee schedule fully funded in the plan
Delivery and permits	Permit status in the data room; independent engineer (optional)
Legal and regulatory: private placement, off-plan rules, assignment of contracts	Counsel review before signing; developer and landlord consent mechanics defined
Currency and FX: EGP returns; USD value may fall	USD equivalents shown at EGP 48; foreign investors take FX advice
Concentration: single project	No cross-collateral or cross-default with other Jalour projects; investor exposed to this project only

Source: Jalour; full risk factors in the Investment Memorandum and the Due Diligence Memorandum.

Timeline and milestones



- Funding and signing: month 3 (ticket due when the down payment of EGP 80 million falls due).
- Option A: units are allocated at signing and delivered at handover (month 48); the investor may resell after consents.
- Option B: 24-month grace, then 12 quarterly instalments from month 30.

Source: Jalour financial model; Financial Annex. Months count from the start of the model timeline.

The ask and next steps

Jalour invites an investment of EGP 50 million in Green Square, with the choice of Option A (units, 2.0x face value) or Option B (cash, 2.3x over 3 years after a 24-month grace period).

- 1 Review this presentation, the Investment Memorandum and the Financial Annex
- 2 Select Option A or Option B and confirm the ticket
- 3 Due diligence: data room, legal and technical review
- 4 Landlord consent and definitive documents
- 5 Signing and funding

Jalour may raise further capital at project or holding level, subject to the investor's stated rights. Projections are not guarantees. All information in this presentation and in the other documents of this pack is confidential and subject to the non-disclosure agreement.
